Group Outcomes

- Sprint goal, product backlog tasks and volunteers are in the excel spreadsheet
- SMART sprint goal: Finalize a second client and create frameworks for all main pages. Create a database and impliment sign up and sign in feature.
- Burndown Chart (Talk to you about making it better and will be updated by next sprint)
  - 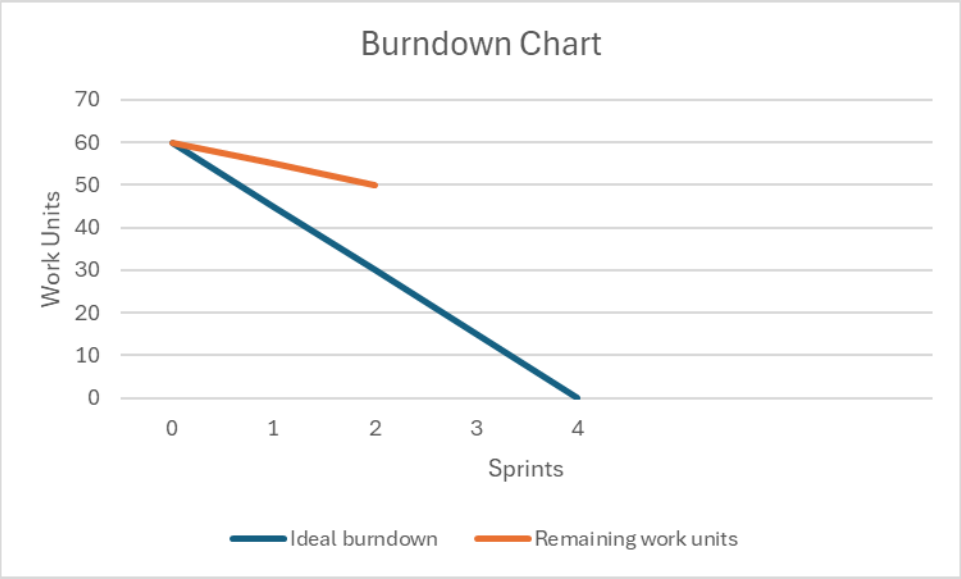

- UML Diagram

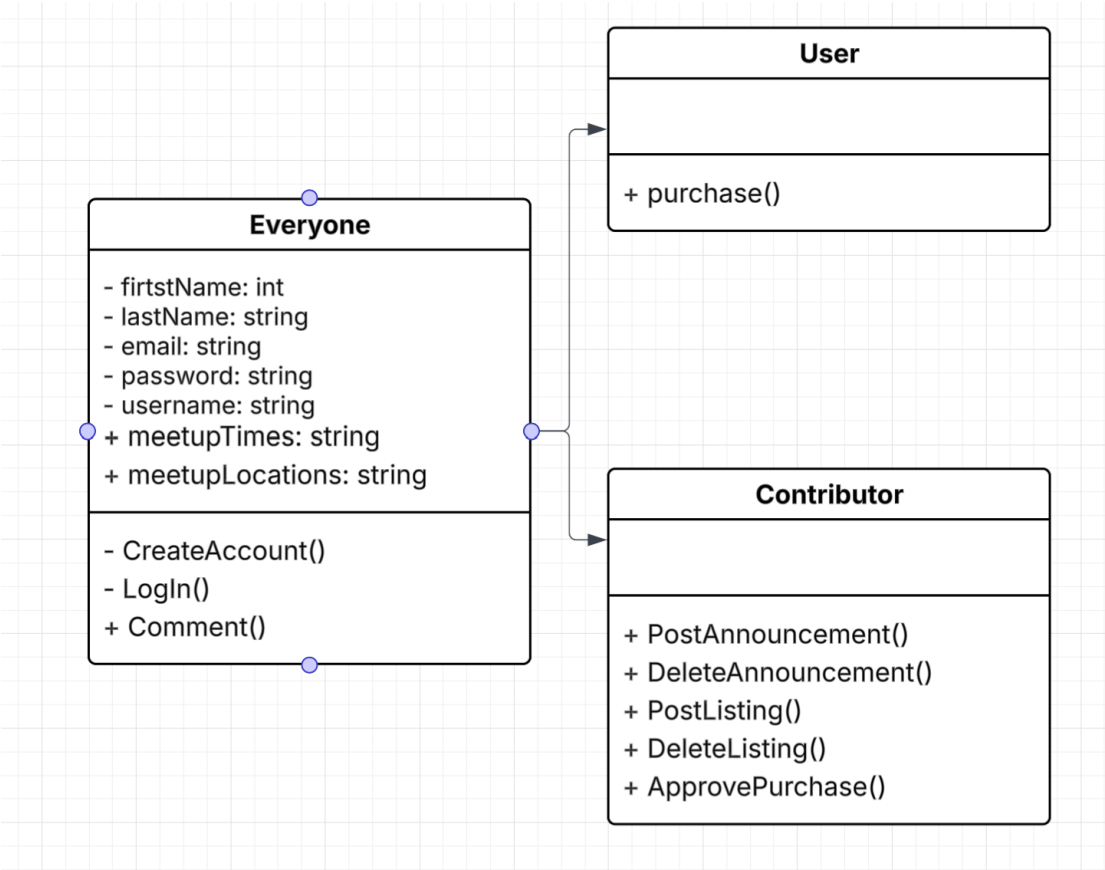

- Was the sprint goal accomplished?
    - The sprint goal was mostly accomplished. We pivoted after learning some class expectaions from getting a baseline for all the features mostly through styling and format to focusing on one feature. Due to this we didn't get all of the styling and format done for all the pages
- What changes would you recommend for work on the next sprint?
    - Next sprint we will focus more on one or two features rather than an overarching goal like this time. We will also spread out our work more.
- Look at some other groups' projects and web pages?
    - Tried to look at everyone's website but could only access project 4 without downloading files. I admire the design of project 4's website as it matches well with their subject. Project 2 has very thorough and well organized documentation.

Member participation

- Scrum Meeting Notes
    - 2/11/26

    - Did not do standup. We were doing our sprint 1 demo and talking to Prof. DeFrance
    -
    - 2/13/26
        - Sylvia dmd ihos and it has not been opened
        - We need to pivot and find a new person to reach out to
        - Find new person
        - Today work on homepage together
        - Finish beginning of sprint
    -
    - 2/18/26
        - We have not recieved an email from black pearl tea house
        - Sylvia made new uml diagram
        - Sylvia made outline for sprint 2 retrospective
        - Sylvia dm black pearl
        - Kaylee figure out tailwind
        - Sylvia get MUI installed
        - Sylvia make header
        - Sylvia needs to make page to showcase page
        - Sylvia needs to make shop page
        - Kaylee needs to update documentation
        - Kaylee needs to create community page
        - Sylvia find a way to host the webpage
        - We need to have a way to login
        - Kaylee: 1
        - Sylvia: 2
- Work log is on Sprint 2 Backlog page
- Would you have spent the time differently? How?
    - Yes we would have focused more on a single or a few features from the start rather than design. We should have researched all the tools we would need sooner.
